WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 1	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Bead	28mm
Sash Type	Casement right hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Vertical Split Position	By Dimensions



Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	604	[-]		
Vert	Bead	28mm Bead	2	1138.5	[-]		
Hor	Bead	28mm Bead	2	502	[-]		
Vert	Bead	28mm Bead	2	236.5	[-]		
Hor	Frame	Frame 6 Chamber	2	705	\ - /		
Vert	Frame	Frame 6 Chamber	1	405	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	1205	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	1205	[Y - /		
Vert	Frame	Frame 6 Chamber	1	405	[Y - /		
Hor	Frame	Chasement Z Sash	1	703	< - >		
Hor	Sash	T Sash	2	625	\ - /	28 x 24 Steel Reinforcement	462
Vert	Sash	T Sash	2	359.5	\ - /	28 x 24 Steel Reinforcement	196.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	1	Unit
Gasket 02	4.882	Metres
Glazing Bridge Packer	13	Unit
Gasket 01	3.898	Metres
White Inline Handle	1	Unit
200mm Espagnolette	1	Unit
16” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	492	226
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	594	1128

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 2	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Sash
Drainage	Concealed Drainage
Location	Please Specify

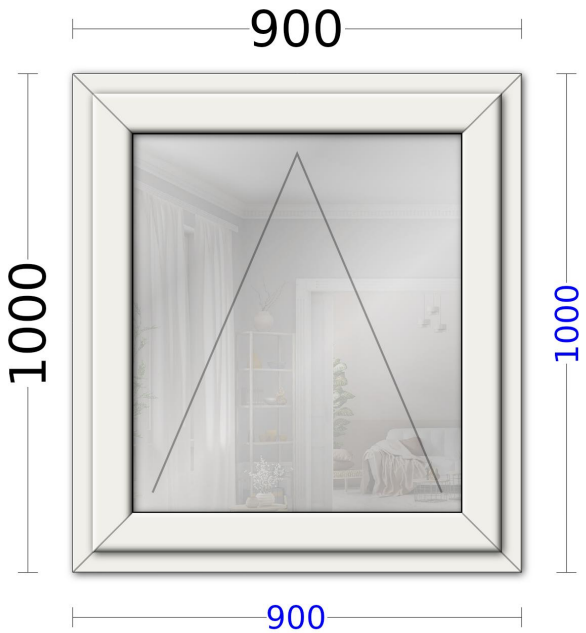

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	702	[-]		
Vert	Bead	28mm Bead	2	802	[-]		
Hor	Frame	Frame 6 Chamber	2	905	\ - /		
Vert	Frame	Frame 6 Chamber	2	1005	\ - /		
Hor	Sash	T Sash	2	825	\ - /	28 x 24 Steel Reinforcement	662
Vert	Sash	T Sash	2	925	\ - /	28 x 24 Steel Reinforcement	762

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 01	6.96	Metres
White Inline Handle	1	Unit
600mm Espagnolette	1	Unit
24” Friction Hinge	1	Unit
Gasket 02	2.968	Metres
Glazing Bridge Packer	8	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	692	792

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 3	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Bead	28mm
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify



Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	704	[-]		
Vert	Bead	28mm Bead	2	904	[-]		
Hor	Frame	Frame 6 Chamber	2	805	\ - /		
Vert	Frame	Frame 6 Chamber	2	1005	\ - /		

Accessories Required:	Qty	Unit Of Measurement
Gasket 02	3.176	Metres
Glazing Bridge Packer	5	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	694	894

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 4	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Sash
Drainage	Concealed Drainage
Location	Please Specify



Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	502	[-]		
Vert	Bead	28mm Bead	2	1002	[-]		
Hor	Frame	Frame 6 Chamber	2	705	\ - /		
Vert	Frame	Frame 6 Chamber	2	1205	\ - /		
Hor	Sash	T Sash	2	625	\ - /	28 x 24 Steel Reinforcement	462
Vert	Sash	T Sash	2	1125	\ - /	28 x 24 Steel Reinforcement	962


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	4	Unit
Run Up Block	1	Unit
Gasket 01	6.96	Metres
White Inline Handle	1	Unit
1000mm Espagnolette	1	Unit
16” Friction Hinge	1	Unit
Gasket 02	2.968	Metres
Glazing Bridge Packer	8	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	492	992

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 5	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Bead	28mm
Sash Type	Casement right hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Sash
Drainage	Concealed Drainage
Location	Please Specify

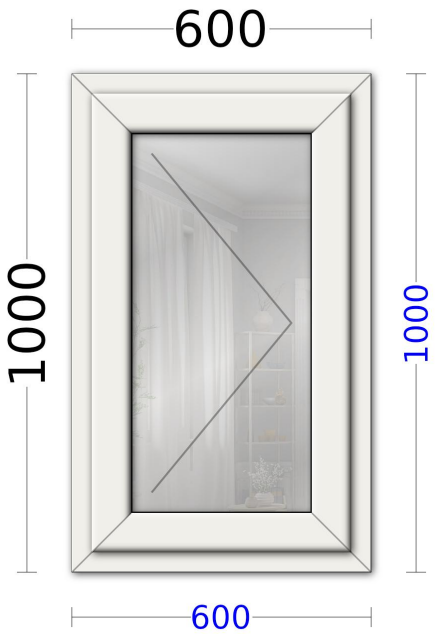

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	402	[-]		
Vert	Bead	28mm Bead	2	802	[-]		
Hor	Frame	Frame 6 Chamber	2	605	\ - /		
Vert	Frame	Frame 6 Chamber	2	1005	\ - /		
Hor	Sash	T Sash	2	525	\ - /	28 x 24 Steel Reinforcement	362
Vert	Sash	T Sash	2	925	\ - /	28 x 24 Steel Reinforcement	762


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	1	Unit
Gasket 01	5.76	Metres
White Inline Handle	1	Unit
800mm Espagnolette	1	Unit
12” Friction Hinge	1	Unit
Gasket 02	2.368	Metres
Glazing Bridge Packer	8	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	392	792

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 6	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Bead	28mm
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Vertical Split Position	By Dimensions

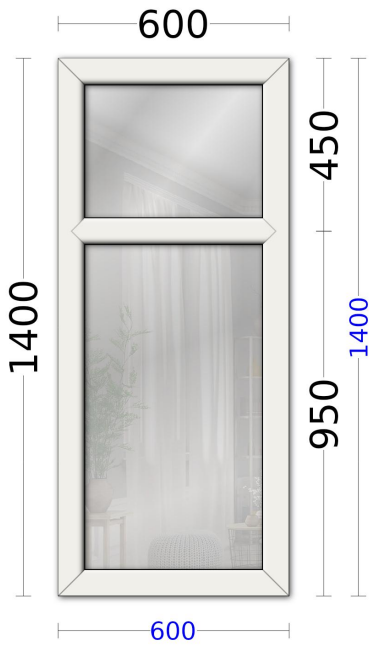

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	4	504	[-]		
Vert	Bead	28mm Bead	2	888.5	[-]		
Vert	Bead	28mm Bead	2	388.5	[-]		
Hor	Frame	Frame 6 Chamber	2	605	\ - /		
Vert	Frame	Frame 6 Chamber	2	1405	\ - /		
Hor	Frame	Chasement T Sash	1	603	< - >		


Accessories Required:	Qty	Unit Of Measurement
Gasket 02	4.49	Metres
Glazing Bridge Packer	10	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	494	378
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	494	878

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 7	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Vertical Split Position	By Dimensions

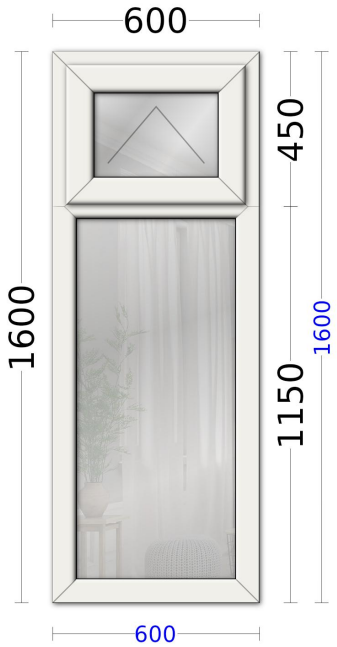

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	504	[-]		
Vert	Bead	28mm Bead	2	1088.5	[-]		
Hor	Bead	28mm Bead	2	402	[-]		
Vert	Bead	28mm Bead	2	286.5	[-]		
Hor	Frame	Frame 6 Chamber	2	605	\ - /		
Vert	Frame	Frame 6 Chamber	1	455	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	1155	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	1155	[Y - /		
Vert	Frame	Frame 6 Chamber	1	455	[Y - /		
Hor	Frame	Chasement Z Sash	1	603	< - >		
Hor	Sash	T Sash	2	525	\ - /	28 x 24 Steel Reinforcement	362
Vert	Sash	T Sash	2	409.5	\ - /	28 x 24 Steel Reinforcement	246.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	4.482	Metres
Glazing Bridge Packer	13	Unit
Gasket 01	3.698	Metres
White Inline Handle	1	Unit
400mm Espagnolette	1	Unit
10” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	392	276
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	494	1078

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 8	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Sash
Drainage	Concealed Drainage
Location	Please Specify
Vertical Split Position	By Dimensions

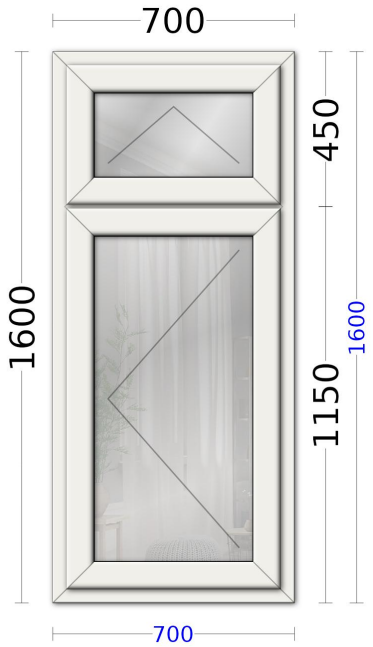

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	4	502	[-]		
Vert	Bead	28mm Bead	2	286.5	[-]		
Vert	Bead	28mm Bead	2	986.5	[-]		
Hor	Frame	Frame 6 Chamber	2	705	\ - /		
Vert	Frame	Frame 6 Chamber	2	1605	\ - /		
Hor	Frame	Chasement T Sash	1	703	< - >		
Hor	Sash	T Sash	4	625	\ - /	28 x 24 Steel Reinforcement	462
Vert	Sash	T Sash	2	409.5	\ - /	28 x 24 Steel Reinforcement	246.5
Vert	Sash	T Sash	2	1109.5	\ - /	28 x 24 Steel Reinforcement	946.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	6	Unit
Run Up Block	3	Unit
Gasket 01	10.996	Metres
White Inline Handle	2	Unit
400mm Espagnolette	1	Unit
10” Friction Hinge	1	Unit
Gasket 02	4.474	Metres
Glazing Bridge Packer	16	Unit
1000mm Espagnolette	1	Unit
16” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	492	276
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	492	976

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 9	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung right hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Sash
Drainage	Concealed Drainage
Location	Please Specify
Vertical Split Position	By Dimensions

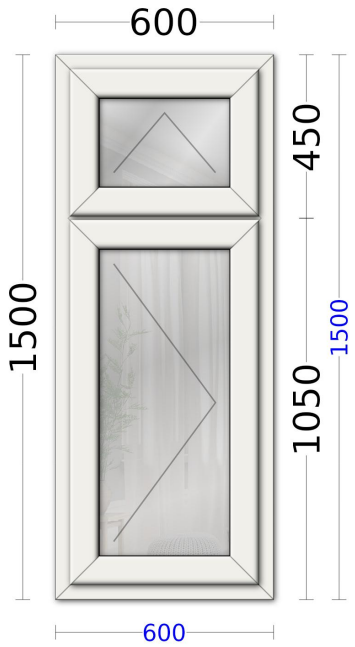

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	4	402	[-]		
Vert	Bead	28mm Bead	2	286.5	[-]		
Vert	Bead	28mm Bead	2	886.5	[-]		
Hor	Frame	Frame 6 Chamber	2	605	\ - /		
Vert	Frame	Frame 6 Chamber	2	1505	\ - /		
Hor	Frame	Chasement T Sash	1	603	< - >		
Hor	Sash	T Sash	4	525	\ - /	28 x 24 Steel Reinforcement	362
Vert	Sash	T Sash	2	409.5	\ - /	28 x 24 Steel Reinforcement	246.5
Vert	Sash	T Sash	2	1009.5	\ - /	28 x 24 Steel Reinforcement	846.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	4	Unit
Run Up Block	3	Unit
Gasket 01	9.796	Metres
White Inline Handle	2	Unit
400mm Espagnolette	1	Unit
10” Friction Hinge	1	Unit
Gasket 02	3.874	Metres
Glazing Bridge Packer	16	Unit
800mm Espagnolette	1	Unit
12” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	392	276
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	392	876

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 10	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions

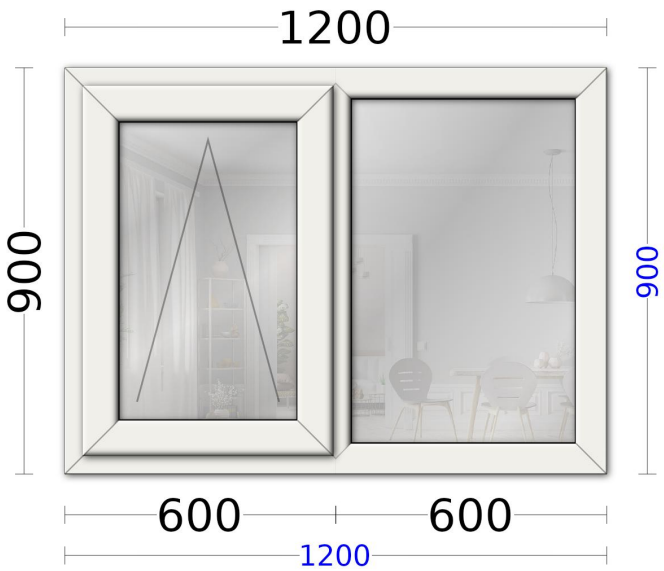

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	2	804	[-]		
Hor	Bead	28mm Bead	2	538.5	[-]		
Vert	Bead	28mm Bead	2	702	[-]		
Hor	Bead	28mm Bead	2	436.5	[-]		
Hor	Frame	Frame 6 Chamber	2	605	\ - Y]		
Vert	Frame	Frame 6 Chamber	2	905	\ - /		
Hor	Frame	Frame 6 Chamber	2	605	[Y - /		
Hor	Frame	Chasement Z Sash	1	903	< - >		
Vert	Sash	T Sash	2	825	\ - /	28 x 24 Steel Reinforcement	662
Hor	Sash	T Sash	2	559.5	\ - /	28 x 24 Steel Reinforcement	396.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	4.882	Metres
Glazing Bridge Packer	13	Unit
Gasket 01	5.498	Metres
White Inline Handle	1	Unit
400mm Espagnolette	1	Unit
24” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	426	692
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	528	794

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 11	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions

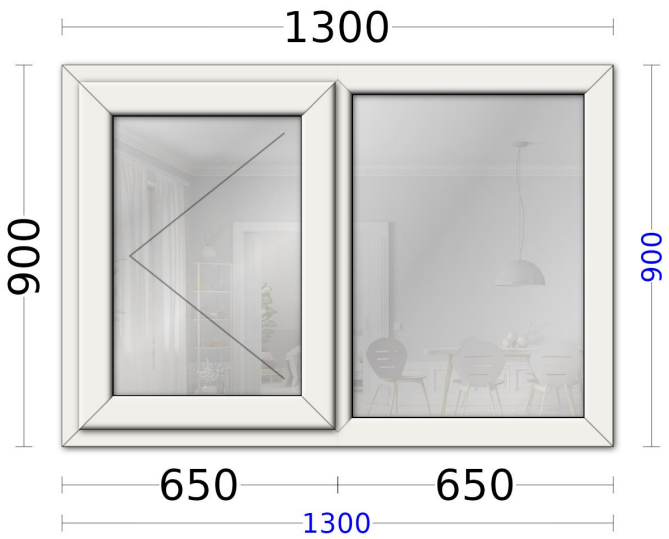

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	2	804	[-]		
Hor	Bead	28mm Bead	2	588.5	[-]		
Vert	Bead	28mm Bead	2	702	[-]		
Hor	Bead	28mm Bead	2	486.5	[-]		
Hor	Frame	Frame 6 Chamber	2	655	\ - Y]		
Vert	Frame	Frame 6 Chamber	2	905	\ - /		
Hor	Frame	Frame 6 Chamber	2	655	[Y - /		
Hor	Frame	Chasement Z Sash	1	903	< - >		
Vert	Sash	T Sash	2	825	\ - /	28 x 24 Steel Reinforcement	662
Hor	Sash	T Sash	2	609.5	\ - /	28 x 24 Steel Reinforcement	446.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	1	Unit
Gasket 02	5.082	Metres
Glazing Bridge Packer	13	Unit
Gasket 01	5.698	Metres
White Inline Handle	1	Unit
600mm Espagnolette	1	Unit
16” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	476	692
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	578	794

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 12	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Sash
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions

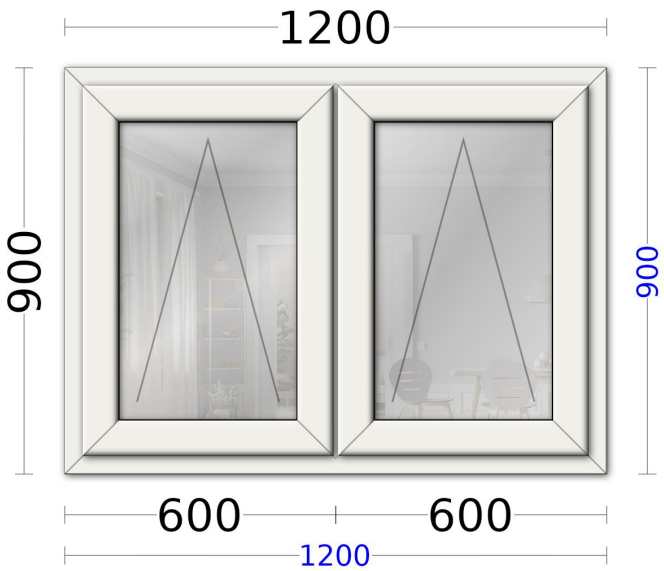

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	4	702	[-]		
Hor	Bead	28mm Bead	4	436.5	[-]		
Hor	Frame	Frame 6 Chamber	2	1205	\ - /		
Vert	Frame	Frame 6 Chamber	2	905	\ - /		
Hor	Frame	Chasement T Sash	1	903	< - >		
Vert	Sash	T Sash	4	825	\ - /	28 x 24 Steel Reinforcement	662
Hor	Sash	T Sash	4	559.5	\ - /	28 x 24 Steel Reinforcement	396.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	4	Unit
Run Up Block	4	Unit
Gasket 01	10.996	Metres
White Inline Handle	2	Unit
400mm Espagnolette	2	Unit
24” Friction Hinge	2	Unit
Gasket 02	4.474	Metres
Glazing Bridge Packer	16	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	426	692
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	426	692

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 13	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions



Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	2	904	[-]		
Hor	Bead	28mm Bead	2	238.5	[-]		
Vert	Bead	28mm Bead	2	802	[-]		
Hor	Bead	28mm Bead	2	336.5	[-]		
Hor	Frame	Frame 6 Chamber	1	505	\ - Y]		
Hor	Frame	Frame 6 Chamber	1	305	\ - Y]		
Vert	Frame	Frame 6 Chamber	2	1005	\ - /		
Hor	Frame	Frame 6 Chamber	1	305	[Y - /		
Hor	Frame	Frame 6 Chamber	1	505	[Y - /		
Hor	Frame	Chasement Z Sash	1	1003	< - >		
Vert	Sash	T Sash	2	925	\ - /	28 x 24 Steel Reinforcement	762
Hor	Sash	T Sash	2	459.5	\ - /	28 x 24 Steel Reinforcement	296.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	4.482	Metres
Glazing Bridge Packer	13	Unit
Gasket 01	5.498	Metres
White Inline Handle	1	Unit
400mm Espagnolette	1	Unit
24” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	326	792
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	228	894

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 14	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Sash
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions

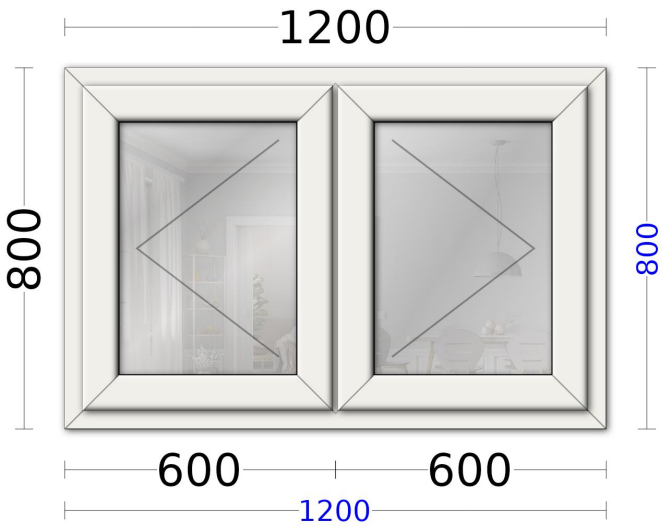

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	4	602	[-]		
Hor	Bead	28mm Bead	4	436.5	[-]		
Hor	Frame	Frame 6 Chamber	2	1205	\ - /		
Vert	Frame	Frame 6 Chamber	2	805	\ - /		
Hor	Frame	Chasement T Sash	1	803	< - >		
Vert	Sash	T Sash	4	725	\ - /	28 x 24 Steel Reinforcement	562
Hor	Sash	T Sash	4	559.5	\ - /	28 x 24 Steel Reinforcement	396.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	4	Unit
Run Up Block	2	Unit
Gasket 01	10.196	Metres
White Inline Handle	2	Unit
600mm Espagnolette	2	Unit
16” Friction Hinge	2	Unit
Gasket 02	4.074	Metres
Glazing Bridge Packer	16	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	426	592
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	426	592

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 15	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions

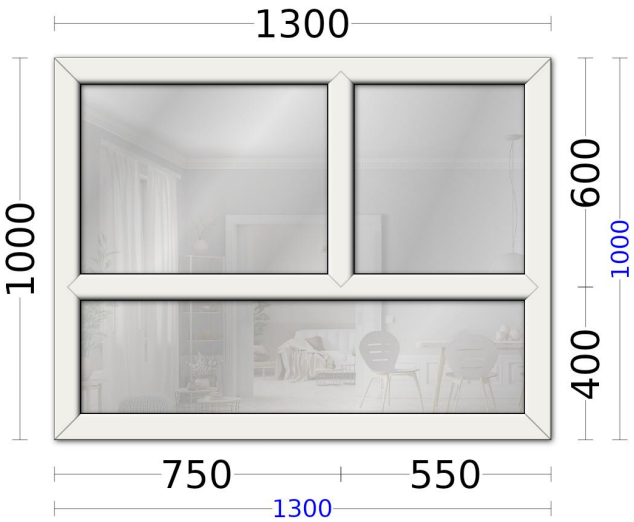

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	1204	[-]		
Vert	Bead	28mm Bead	2	338.5	[-]		
Vert	Bead	28mm Bead	4	538.5	[-]		
Hor	Bead	28mm Bead	2	688.5	[-]		
Hor	Bead	28mm Bead	2	488.5	[-]		
Hor	Frame	Frame 6 Chamber	2	1305	\ - /		
Vert	Frame	Frame 6 Chamber	2	1005	\ - /		
Hor	Frame	Chasement T Sash	1	1303	< - >	13 x 29 Steel Reinforcement	1164
Hor	Frame	Chasement T Sash	1	637.5	< - >		


Accessories Required:	Qty	Unit Of Measurement
Gasket 02	7.473	Metres
Glazing Bridge Packer	15	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	678	528
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	1194	328
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	478	528

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 16	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions

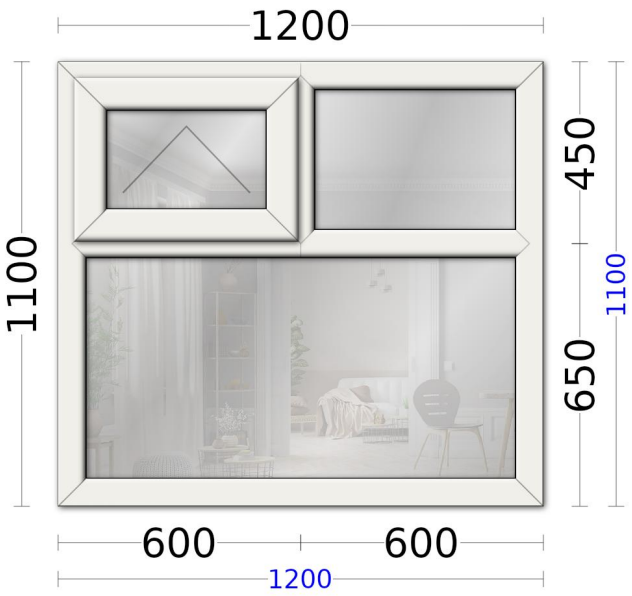

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	1104	[-]		
Vert	Bead	28mm Bead	2	588.5	[-]		
Vert	Bead	28mm Bead	2	388.5	[-]		
Hor	Bead	28mm Bead	2	538.5	[-]		
Vert	Bead	28mm Bead	2	286.5	[-]		
Hor	Bead	28mm Bead	2	436.5	[-]		
Hor	Frame	Frame 6 Chamber	2	605	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	1105	\ - /		
Hor	Frame	Frame 6 Chamber	1	1205	\ - /		
Vert	Frame	Frame 6 Chamber	1	655	[Y - /		
Vert	Frame	Frame 6 Chamber	1	455	[Y - /		
Hor	Frame	Chasement Z Sash	1	604	[Y - >	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement T Sash	1	604	< - Y]	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement Z Sash	1	487.5	< - >		
Vert	Sash	T Sash	2	409.5	\ - /	28 x 24 Steel Reinforcement	246.5
Hor	Sash	T Sash	2	559.5	\ - /	28 x 24 Steel Reinforcement	396.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	6.565	Metres
Glazing Bridge Packer	18	Unit
Gasket 01	3.836	Metres
White Inline Handle	1	Unit
400mm Espagnolette	1	Unit
10” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	426	276
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	1094	578

WORK ORDER


Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 17	Print Info:	11/8/2026

Glass Required:	**Qty**	**Width**	**Length**
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	528	378

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 18	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions

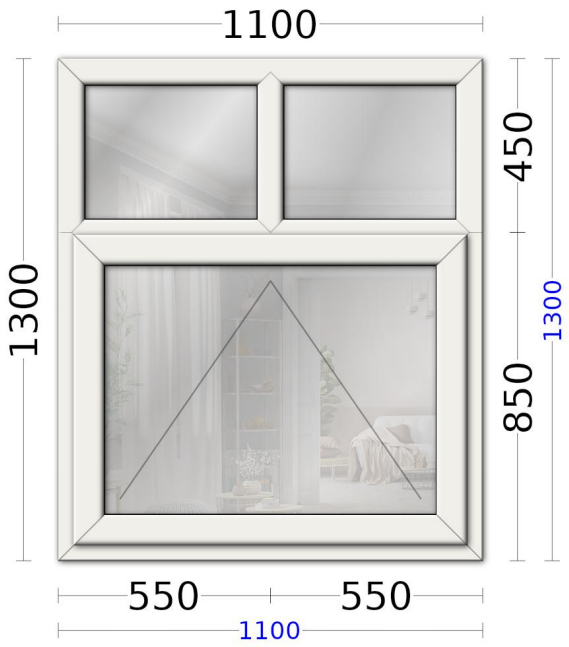

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	4	388.5	[-]		
Hor	Bead	28mm Bead	4	488.5	[-]		
Hor	Bead	28mm Bead	2	902	[-]		
Vert	Bead	28mm Bead	2	686.5	[-]		
Hor	Frame	Frame 6 Chamber	2	1105	\ - /		
Vert	Frame	Frame 6 Chamber	1	455	[Y - /		
Vert	Frame	Frame 6 Chamber	1	855	[Y - /		
Vert	Frame	Frame 6 Chamber	1	855	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	455	\ - Y]		
Hor	Frame	Chasement Z Sash	1	1103	< - >	13 x 29 Steel Reinforcement	964
Hor	Frame	Chasement T Sash	1	487.5	< - >		
Hor	Sash	T Sash	2	1025	\ - /	28 x 24 Steel Reinforcement	862
Vert	Sash	T Sash	2	809.5	\ - /	28 x 24 Steel Reinforcement	646.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	6.565	Metres
Glazing Bridge Packer	18	Unit
Gasket 01	7.298	Metres
White Inline Handle	1	Unit
800mm Espagnolette	1	Unit
24” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	478	378
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	892	676
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	478	378

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 19	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions

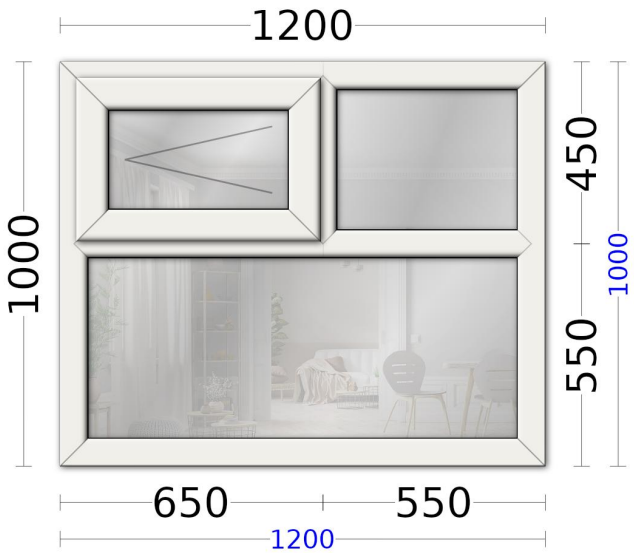

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	1104	[-]		
Vert	Bead	28mm Bead	2	488.5	[-]		
Vert	Bead	28mm Bead	2	388.5	[-]		
Hor	Bead	28mm Bead	2	488.5	[-]		
Vert	Bead	28mm Bead	2	286.5	[-]		
Hor	Bead	28mm Bead	2	486.5	[-]		
Hor	Frame	Frame 6 Chamber	1	655	\ - Y]		
Hor	Frame	Frame 6 Chamber	1	555	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	1005	\ - /		
Hor	Frame	Frame 6 Chamber	1	1205	\ - /		
Vert	Frame	Frame 6 Chamber	1	555	[Y - /		
Vert	Frame	Frame 6 Chamber	1	455	[Y - /		
Hor	Frame	Chasement Z Sash	1	654	[Y - >	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement T Sash	1	554	< - Y]	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement Z Sash	1	487.5	< - >		
Vert	Sash	T Sash	2	409.5	\ - /	28 x 24 Steel Reinforcement	246.5
Hor	Sash	T Sash	2	609.5	\ - /	28 x 24 Steel Reinforcement	446.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	1	Unit
Gasket 02	6.365	Metres
Glazing Bridge Packer	18	Unit
Gasket 01	4.0360003	Metres
White Inline Handle	1	Unit
200mm Espagnolette	1	Unit
16” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	476	276

WORK ORDER


Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 20	Print Info:	11/8/2026

Glass Required:	**Qty**	**Width**	**Length**
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	1094	478
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	478	378

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 21	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions

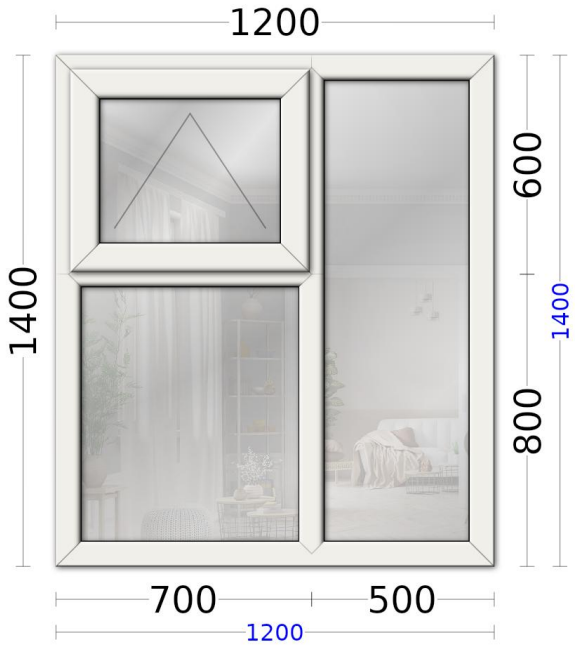

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	2	1304	[-]		
Hor	Bead	28mm Bead	2	438.5	[-]		
Hor	Bead	28mm Bead	2	638.5	[-]		
Vert	Bead	28mm Bead	2	738.5	[-]		
Hor	Bead	28mm Bead	2	536.5	[-]		
Vert	Bead	28mm Bead	2	436.5	[-]		
Hor	Frame	Frame 6 Chamber	1	705	\ - Y]		
Hor	Frame	Frame 6 Chamber	1	505	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	1405	\ - /		
Hor	Frame	Frame 6 Chamber	1	1205	\ - /		
Vert	Frame	Frame 6 Chamber	1	805	[Y - /		
Vert	Frame	Frame 6 Chamber	1	605	[Y - /		
Hor	Frame	Chasement Z Sash	1	604	< - Y]	13 x 29 Steel Reinforcement	1264
Hor	Frame	Chasement T Sash	1	804	< - Y]	13 x 29 Steel Reinforcement	1264
Hor	Frame	Chasement Z Sash	1	737.5	< - >		
Hor	Sash	T Sash	2	659.5	\ - /	28 x 24 Steel Reinforcement	496.5
Vert	Sash	T Sash	2	559.5	\ - /	28 x 24 Steel Reinforcement	396.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	8.065	Metres
Glazing Bridge Packer	18	Unit
Gasket 01	4.836	Metres
White Inline Handle	1	Unit
600mm Espagnolette	1	Unit
16” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	526	426

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 22	Print Info:	11/8/2026

Glass Required:	**Qty**	**Width**	**Length**
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	628	728
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	428	1294

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 23	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement right hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions



Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	4	588.5	[-]		
Vert	Bead	28mm Bead	2	688.5	[-]		
Vert	Bead	28mm Bead	2	388.5	[-]		
Vert	Bead	28mm Bead	2	1002	[-]		
Hor	Bead	28mm Bead	2	486.5	[-]		
Hor	Frame	Frame 6 Chamber	2	655	[Y - /		
Vert	Frame	Frame 6 Chamber	2	1205	\ - /		
Hor	Frame	Frame 6 Chamber	2	655	\ - Y]		
Hor	Frame	Chasement Z Sash	1	1203	< - >	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement T Sash	1	687.5	< - >		
Vert	Sash	T Sash	2	1125	\ - /	28 x 24 Steel Reinforcement	962
Hor	Sash	T Sash	2	609.5	\ - /	28 x 24 Steel Reinforcement	446.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	4	Unit
Run Up Block	1	Unit
Gasket 02	7.365	Metres
Glazing Bridge Packer	18	Unit
Gasket 01	6.898	Metres
White Inline Handle	1	Unit
1000mm Espagnolette	1	Unit
16” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	578	378
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	578	678
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	476	992

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 24	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions



Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	4	904	[-]		
Hor	Bead	28mm Bead	2	423	[-]		
Hor	Bead	28mm Bead	2	388.5	[-]		
Vert	Bead	28mm Bead	2	802	[-]		
Hor	Bead	28mm Bead	2	436.5	[-]		
Hor	Frame	Frame 6 Chamber	1	605	\ - Y]		
Hor	Frame	Frame 6 Chamber	1	905	\ - Y]		
Vert	Frame	Frame 6 Chamber	2	1005	\ - /		
Hor	Frame	Frame 6 Chamber	1	905	[Y - /		
Hor	Frame	Frame 6 Chamber	1	605	[Y - /		
Hor	Frame	Chasement Z Sash	1	1003	< - >		
Hor	Frame	Chasement T Sash	1	1003	< - >		
Vert	Sash	T Sash	2	925	\ - /	28 x 24 Steel Reinforcement	762
Hor	Sash	T Sash	2	559.5	\ - /	28 x 24 Steel Reinforcement	396.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	7.5959997	Metres
Glazing Bridge Packer	18	Unit
Gasket 01	5.898	Metres
White Inline Handle	1	Unit
400mm Espagnolette	1	Unit
24” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	426	792
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	413	894
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	378	894

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 25	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions

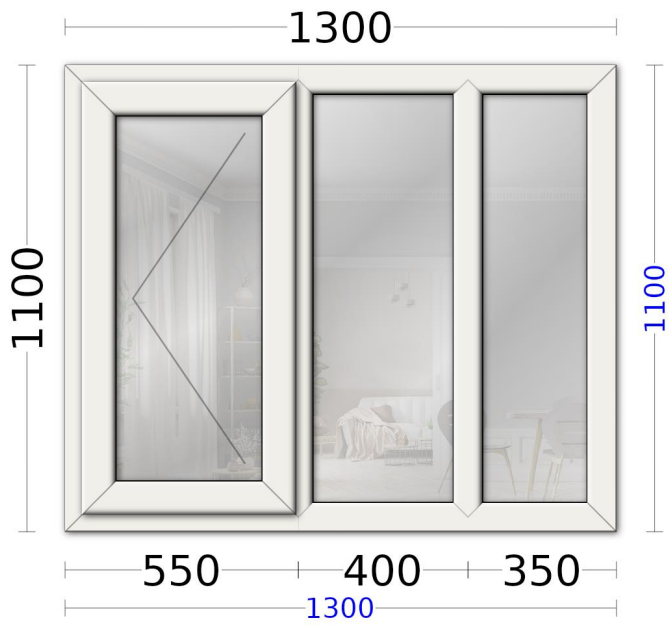

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	4	1004	[-]		
Hor	Bead	28mm Bead	2	373	[-]		
Hor	Bead	28mm Bead	2	288.5	[-]		
Vert	Bead	28mm Bead	2	902	[-]		
Hor	Bead	28mm Bead	2	386.5	[-]		
Hor	Frame	Frame 6 Chamber	1	555	\ - Y]		
Hor	Frame	Frame 6 Chamber	1	755	\ - Y]		
Vert	Frame	Frame 6 Chamber	2	1105	\ - /		
Hor	Frame	Frame 6 Chamber	1	755	[Y - /		
Hor	Frame	Frame 6 Chamber	1	555	[Y - /		
Hor	Frame	Chasement Z Sash	1	1103	< - >	13 x 29 Steel Reinforcement	964
Hor	Frame	Chasement T Sash	1	1103	< - >	13 x 29 Steel Reinforcement	964
Vert	Sash	T Sash	2	1025	\ - /	28 x 24 Steel Reinforcement	862
Hor	Sash	T Sash	2	509.5	\ - /	28 x 24 Steel Reinforcement	346.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	1	Unit
Gasket 02	7.796	Metres
Glazing Bridge Packer	18	Unit
Gasket 01	6.0979996	Metres
White Inline Handle	1	Unit
800mm Espagnolette	1	Unit
12” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	376	892
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	363	994
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	278	994

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 26	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions



Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	2	1104	[-]		
Hor	Bead	28mm Bead	2	373	[-]		
Vert	Bead	28mm Bead	4	1002	[-]		
Hor	Bead	28mm Bead	4	386.5	[-]		
Hor	Frame	Frame 6 Chamber	2	555	\ - Y]		
Hor	Frame	Frame 6 Chamber	2	405	[Y - Y]		
Hor	Frame	Frame 6 Chamber	2	555	[Y - /		
Vert	Frame	Frame 6 Chamber	2	1205	\ - /		
Hor	Frame	Chasement Z Sash	2	1203	< - >	13 x 29 Steel Reinforcement	1064
Vert	Sash	T Sash	4	1125	\ - /	28 x 24 Steel Reinforcement	962
Hor	Sash	T Sash	4	509.5	\ - /	28 x 24 Steel Reinforcement	346.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	8	Unit
Run Up Block	2	Unit
Gasket 02	8.388	Metres
Glazing Bridge Packer	21	Unit
Gasket 01	12.996	Metres
White Inline Handle	2	Unit
1000mm Espagnolette	2	Unit
12” Friction Hinge	2	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	376	992
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	363	1094
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	376	992

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 27	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions

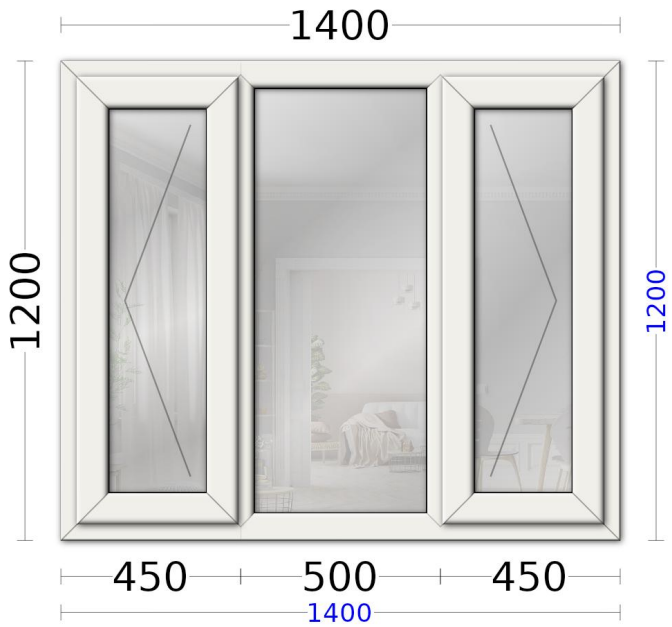

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	2	1104	[-]		
Hor	Bead	28mm Bead	2	473	[-]		
Vert	Bead	28mm Bead	4	1002	[-]		
Hor	Bead	28mm Bead	4	286.5	[-]		
Hor	Frame	Frame 6 Chamber	2	455	\ - Y]		
Hor	Frame	Frame 6 Chamber	2	505	[Y - Y]		
Hor	Frame	Frame 6 Chamber	2	455	[Y - /		
Vert	Frame	Frame 6 Chamber	2	1205	\ - /		
Hor	Frame	Chasement Z Sash	2	1203	< - >	13 x 29 Steel Reinforcement	1064
Vert	Sash	T Sash	4	1125	\ - /	28 x 24 Steel Reinforcement	962
Hor	Sash	T Sash	4	409.5	\ - /	28 x 24 Steel Reinforcement	246.5


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	8	Unit
Run Up Block	2	Unit
Gasket 02	8.188	Metres
Glazing Bridge Packer	21	Unit
Gasket 01	12.196	Metres
White Inline Handle	2	Unit
1000mm Espagnolette	2	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	276	992
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	463	1094
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	276	992

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 28	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions

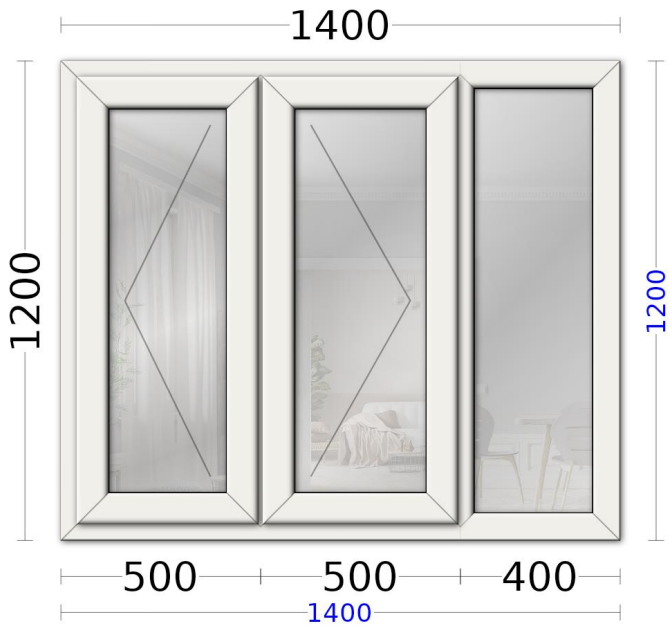

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	2	1104	[-]		
Hor	Bead	28mm Bead	2	338.5	[-]		
Vert	Bead	28mm Bead	4	1002	[-]		
Hor	Bead	28mm Bead	2	336.5	[-]		
Hor	Bead	28mm Bead	2	371	[-]		
Hor	Frame	Frame 6 Chamber	1	1005	\ - Y]		
Hor	Frame	Frame 6 Chamber	1	405	\ - Y]		
Vert	Frame	Frame 6 Chamber	2	1205	\ - /		
Hor	Frame	Frame 6 Chamber	1	405	[Y - /		
Hor	Frame	Frame 6 Chamber	1	1005	[Y - /		
Hor	Frame	Chasement T Sash	1	1203	< - >	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement Z Sash	1	1203	< - >	13 x 29 Steel Reinforcement	1064
Vert	Sash	T Sash	4	1125	\ - /	28 x 24 Steel Reinforcement	962
Hor	Sash	T Sash	2	459.5	\ - /	28 x 24 Steel Reinforcement	296.5
Hor	Sash	T Sash	2	494	\ - /	28 x 24 Steel Reinforcement	331

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	8	Unit
Run Up Block	2	Unit
Gasket 02	8.188	Metres
Glazing Bridge Packer	21	Unit
Gasket 01	12.734	Metres
White Inline Handle	2	Unit
1000mm Espagnolette	2	Unit
12” Friction Hinge	2	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	326	992
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	361	992
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	328	1094

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 29	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions



Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	4	1004	[-]		
Hor	Bead	28mm Bead	2	438.5	[-]		
Hor	Bead	28mm Bead	2	338.5	[-]		
Hor	Bead	28mm Bead	2	473	[-]		
Vert	Bead	28mm Bead	2	538.5	[-]		
Hor	Bead	28mm Bead	2	371	[-]		
Vert	Bead	28mm Bead	2	336.5	[-]		
Hor	Frame	Frame 6 Chamber	1	505	[Y - /		
Hor	Frame	Frame 6 Chamber	1	505	[Y - Y]		
Hor	Frame	Frame 6 Chamber	1	405	\ - Y]		
Vert	Frame	Frame 6 Chamber	2	1105	\ - /		
Hor	Frame	Frame 6 Chamber	1	1405	\ - /		
Hor	Frame	Chasement Z Sash	1	504	[Y - >	13 x 29 Steel Reinforcement	964
Hor	Frame	Chasement T Sash	2	604	< - Y]	13 x 29 Steel Reinforcement	964
Hor	Frame	Chasement Z Sash	1	504	< - Y]	13 x 29 Steel Reinforcement	964
Hor	Frame	Chasement Z Sash	1	572	< - >		
Hor	Sash	T Sash	2	494	\ - /	28 x 24 Steel Reinforcement	331
Vert	Sash	T Sash	2	459.5	\ - /	28 x 24 Steel Reinforcement	296.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	8.848001	Metres
Glazing Bridge Packer	23	Unit
Gasket 01	3.774	Metres
White Inline Handle	1	Unit
400mm Espagnolette	1	Unit
12” Friction Hinge	1	Unit

WORK ORDER


Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 30	Print Info:	11/8/2026

Glass Required:	**Qty**	**Width**	**Length**
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	428	994
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	361	326
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	463	528
04 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	328	994

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 31	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement left hung
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions

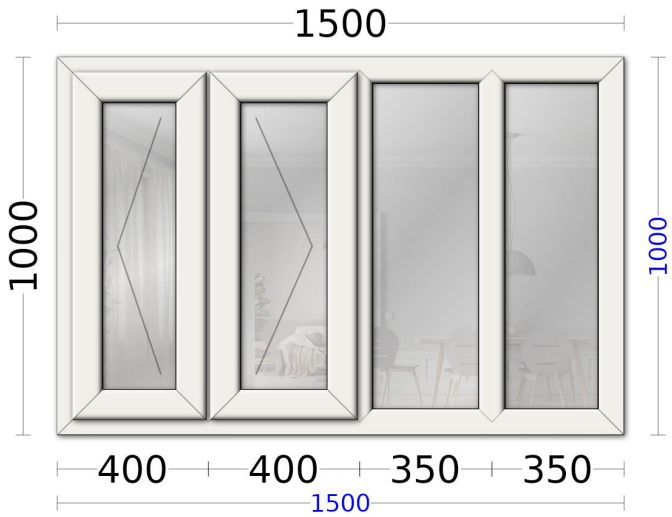

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Vert	Bead	28mm Bead	4	904	[-]		
Hor	Bead	28mm Bead	2	323	[-]		
Hor	Bead	28mm Bead	2	288.5	[-]		
Vert	Bead	28mm Bead	4	802	[-]		
Hor	Bead	28mm Bead	2	236.5	[-]		
Hor	Bead	28mm Bead	2	271	[-]		
Hor	Frame	Frame 6 Chamber	1	805	\ - Y]		
Hor	Frame	Frame 6 Chamber	1	705	\ - Y]		
Vert	Frame	Frame 6 Chamber	2	1005	\ - /		
Hor	Frame	Frame 6 Chamber	1	705	[Y - /		
Hor	Frame	Frame 6 Chamber	1	805	[Y - /		
Hor	Frame	Chasement T Sash	2	1003	< - >		
Hor	Frame	Chasement Z Sash	1	1003	< - >		
Vert	Sash	T Sash	4	925	\ - /	28 x 24 Steel Reinforcement	762
Hor	Sash	T Sash	2	359.5	\ - /	28 x 24 Steel Reinforcement	196.5
Hor	Sash	T Sash	2	394	\ - /	28 x 24 Steel Reinforcement	231


Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	4	Unit
Run Up Block	2	Unit
Gasket 02	8.902	Metres
Glazing Bridge Packer	26	Unit
Gasket 01	10.334	Metres
White Inline Handle	2	Unit
800mm Espagnolette	2	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	226	792
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	261	792
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	313	894
04 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	278	894

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 32	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions

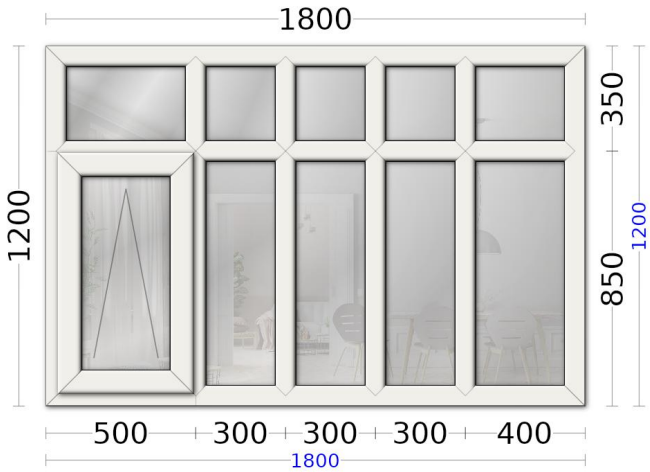

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	2	438.5	[-]		
Vert	Bead	28mm Bead	10	288.5	[-]		
Hor	Bead	28mm Bead	12	273	[-]		
Vert	Bead	28mm Bead	8	788.5	[-]		
Hor	Bead	28mm Bead	4	338.5	[-]		
Hor	Bead	28mm Bead	2	336.5	[-]		
Vert	Bead	28mm Bead	2	686.5	[-]		
Hor	Frame	Frame 6 Chamber	1	1805	\ - /		
Vert	Frame	Frame 6 Chamber	1	1205	\ - /		
Hor	Frame	Frame 6 Chamber	1	1305	[Y - /		
Hor	Frame	Frame 6 Chamber	1	505	[Y - /		
Vert	Frame	Frame 6 Chamber	1	855	\ - Y]		
Vert	Frame	Frame 6 Chamber	1	355	\ - Y]		
Hor	Frame	Chasement T Sash	1	354	[Y - >	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement Z Sash	1	854	[Y - >	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement T Sash	3	1203	< - >	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement Z Sash	1	537.5	< - >		
Hor	Frame	Chasement T Sash	3	372	< - >		
Hor	Frame	Chasement T Sash	1	437.5	< - >		
Hor	Sash	T Sash	2	459.5	\ - /	28 x 24 Steel Reinforcement	296.5
Vert	Sash	T Sash	2	809.5	\ - /	28 x 24 Steel Reinforcement	646.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	16.346	Metres
Glazing Bridge Packer	53	Unit
Gasket 01	5.036	Metres
White Inline Handle	1	Unit

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 33	Print Info:	11/8/2026


Accessories Required:	Qty	Unit Of Measurement
400mm Espagnolette	1	Unit
24” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	428	278
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	326	676
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	278
04 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	778
05 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	278
06 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	778
07 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	278
08 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	778
09 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	328	278
10 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	328	778

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 34	Print Info:	11/8/2026

Main Options	
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions

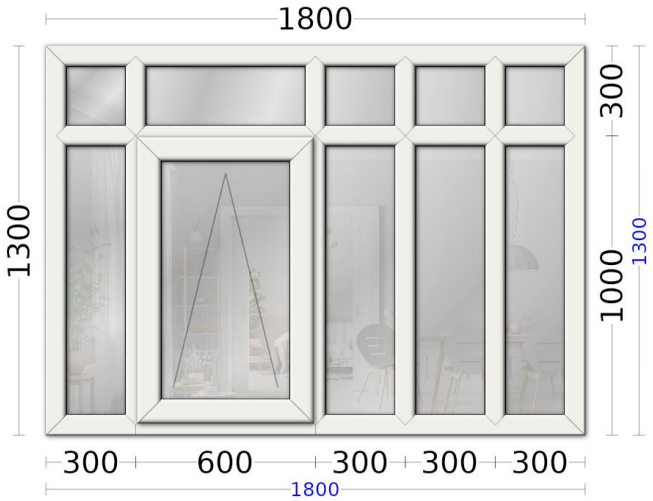

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	8	238.5	[-]		
Vert	Bead	28mm Bead	8	938.5	[-]		
Vert	Bead	28mm Bead	10	238.5	[-]		
Hor	Bead	28mm Bead	2	573	[-]		
Hor	Bead	28mm Bead	8	273	[-]		
Hor	Bead	28mm Bead	2	471	[-]		
Vert	Bead	28mm Bead	2	836.5	[-]		
Hor	Frame	Frame 6 Chamber	1	1805	\ - /		
Vert	Frame	Frame 6 Chamber	2	1305	\ - /		
Hor	Frame	Frame 6 Chamber	1	905	[Y - /		
Hor	Frame	Frame 6 Chamber	1	605	[Y - Y]		
Hor	Frame	Frame 6 Chamber	1	305	\ - Y]		
Hor	Frame	Chasement T Sash	2	304	[Y - >	13 x 29 Steel Reinforcement	1164
Hor	Frame	Chasement Z Sash	1	1004	< - Y]	13 x 29 Steel Reinforcement	1164
Hor	Frame	Chasement Z Sash	1	1004	[Y - >	13 x 29 Steel Reinforcement	1164
Hor	Frame	Chasement T Sash	2	1303	< - >	13 x 29 Steel Reinforcement	1164
Hor	Frame	Chasement T Sash	2	337.5	< - >		
Hor	Frame	Chasement Z Sash	1	672	< - >		
Hor	Frame	Chasement T Sash	2	372	< - >		
Hor	Sash	T Sash	2	594	\ - /	28 x 24 Steel Reinforcement	431
Vert	Sash	T Sash	2	959.5	\ - /	28 x 24 Steel Reinforcement	796.5

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	2	Unit
Run Up Block	2	Unit
Gasket 02	17.346	Metres
Glazing Bridge Packer	53	Unit
Gasket 01	6.174	Metres
White Inline Handle	1	Unit

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 35	Print Info:	11/8/2026


Accessories Required:	Qty	Unit Of Measurement
400mm Espagnolette	1	Unit
24” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	228	228
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	228	928
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	563	228
04 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	461	826
05 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	228
06 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	928
07 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	228
08 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	928
09 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	228	228
10 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	228	928

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 36	Print Info:	11/8/2026

Main Options	
Glass Type	4-20-4 Clear Low E
Glass Gas Fill	Argon
Component Type	Glass
Drainage	Concealed Drainage
Location	Please Specify
Horizontal Split Position	By Dimensions
Vertical Split Position	By Dimensions
Colour (External)	White [SP]
Colour (Internal)	White [SP]
Frame (Standard) (Top)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Bottom)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Left)	SPQ-6-11252 68mm 6 Chamber
Frame (Standard) (Right)	SPQ-6-11252 68mm 6 Chamber
Transom	SPQ-05-20252/SPQ-005-30252 67mm
Mullion	SPQ-05-20252/SPQ-005-30252 67mm
Joint (Structural T/Z) (Transo...	Welded (Standard)
Joint (Structural T/Z) (Mullion)	Welded (Standard)
Bead	28mm
Sash Type	Casement top hung left hand
Locking (Casement)	Espag Locking
Handle (Casement)	White Inline Handle
Hinge (Casement) (S/H)	Standard
Hinge (Casement) (T/H)	Standard
Glass Display Group	Standard
Glazing Method	Glazed

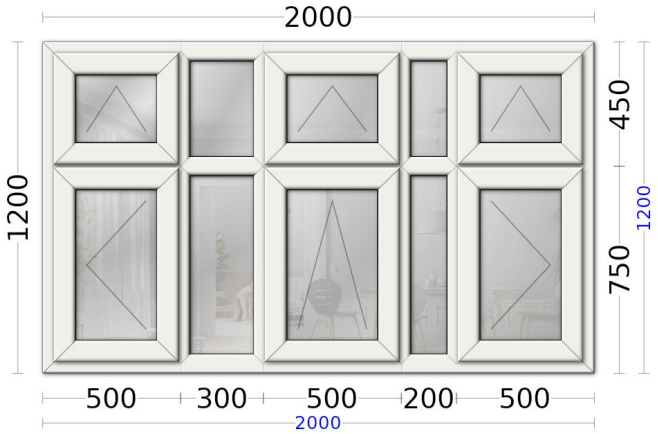

Sections Required:			Qty	Length	End Prep	Reinforcing	Length
Hor	Bead	28mm Bead	4	273	[-]		
Vert	Bead	28mm Bead	4	688.5	[-]		
Vert	Bead	28mm Bead	4	388.5	[-]		
Hor	Bead	28mm Bead	4	173	[-]		
Hor	Bead	28mm Bead	8	336.5	[-]		
Vert	Bead	28mm Bead	6	286.5	[-]		
Vert	Bead	28mm Bead	6	586.5	[-]		
Hor	Bead	28mm Bead	4	371	[-]		
Hor	Frame	Frame 6 Chamber	2	505	\ - Y]		
Hor	Frame	Frame 6 Chamber	2	305	[Y - Y]		
Hor	Frame	Frame 6 Chamber	2	505	[Y - Y]		
Hor	Frame	Frame 6 Chamber	2	205	[Y - Y]		
Hor	Frame	Frame 6 Chamber	2	505	[Y - /		
Vert	Frame	Frame 6 Chamber	2	1205	\ - /		
Hor	Frame	Chasement Z Sash	4	1203	< - >	13 x 29 Steel Reinforcement	1064
Hor	Frame	Chasement T Sash	2	537.5	< - >		
Hor	Frame	Chasement T Sash	1	372	< - >		
Hor	Frame	Chasement T Sash	1	572	< - >		
Hor	Frame	Chasement T Sash	1	272	< - >		
Hor	Sash	T Sash	8	459.5	\ - /	28 x 24 Steel Reinforcement	296.5
Vert	Sash	T Sash	6	409.5	\ - /	28 x 24 Steel Reinforcement	246.5
Vert	Sash	T Sash	6	709.5	\ - /	28 x 24 Steel Reinforcement	546.5
Hor	Sash	T Sash	4	494	\ - /	28 x 24 Steel Reinforcement	331

Accessories Required:	Qty	Unit Of Measurement
Mushroom Striker	12	Unit
Run Up Block	10	Unit
Gasket 02	15.106	Metres

WORK ORDER

Customer:	Test Customer		Input Info:	11/8/2026
Reference:	Ambrish Windows	SupplyAndFit		
Job No:	347	Page 37	Print Info:	11/8/2026

Accessories Required:	Qty	Unit Of Measurement
Glazing Bridge Packer	68	Unit
Gasket 01	24.492	Metres
White Inline Handle	6	Unit
400mm Espagnolette	4	Unit
10” Friction Hinge	3	Unit
600mm Espagnolette	2	Unit
12” Friction Hinge	2	Unit
20” Friction Hinge	1	Unit

Glass Required:	Qty	Width	Length
01 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	326	276
02 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	326	576
03 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	378
04 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	263	678
05 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	361	276
06 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	361	576
07 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	163	378
08 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	163	678
09 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	326	276
10 (Frame-01) 4-20-4 Clear Low E : Thermal Spacer Bar	1	326	576
