# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 1 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | Equal Split |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Vert | Bead | 28mm Bead | 4 | 1550 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 384 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 2 | 1205 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 2 | 1805 | \ - / | | |
| Vert | Sash | Door Sash T | 4 | 1725 | \ - / | 28 x 44.5 U Steel Reinforcement | 1510 |
| Hor | Sash | Door Sash T | 4 | 559 | \ - / | 28 x 44.5 U Steel Reinforcement | 344 |
| Vert | Sash group | French Mullion | 1 | 1638 | [ - ] | 28 x 24 Steel Reinforcement | 1638 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |
| Gasket 01 | 18.192001 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Gasket 02 | 7.656 | Metres |
| Glazing Bridge Packer | 16 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 374 | 1540 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 374 | 1540 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 2 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Transom | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Transo... | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | Equal Split |
| Vertical Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Hor | Bead | 28mm Bead | 2 | 1304 | [ - ] | | |
| Vert | Bead | 28mm Bead | 2 | 383 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1329 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 484 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 2 | 1405 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 455 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 1555 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 1555 | \ - Y] | | |
| Vert | Frame | Frame 6 Chamber | 1 | 455 | \ - Y] | | |
| Hor | Frame | | 1 | 1409 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1504 | \ - / | 28 x 44.5 U Steel Reinforcement | 1289 |
| Hor | Sash | Door Sash T | 4 | 659 | \ - / | 28 x 44.5 U Steel Reinforcement | 444 |
| Vert | Sash group | French Mullion | 1 | 1421 | [ - ] | 28 x 24 Steel Reinforcement | 1421 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 10.506000 | Metres |
| Glazing Bridge Packer | 21 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |
| Gasket 01 | 17.223999 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 3 | Print Info: | 11/5/2026 |

| **Glass Required:** | **Qty** | **Width** | **Length** |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 1294 | 373 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 474 | 1319 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 474 | 1319 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 4 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Transom | SPQ-5-30252 78mm |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Transo... | Welded (Standard) |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |
| Vertical Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Vert | Bead | 28mm Bead | 4 | 333 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 633 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1279 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 484 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 2 | 1405 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 405 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 1505 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 1505 | \ - Y] | | |
| Vert | Frame | Frame 6 Chamber | 1 | 405 | \ - Y] | | |
| Hor | Frame | | 1 | 1409 | < - > | | |
| Hor | Frame | T Transom/Mullion | 1 | 454 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1454 | \ - / | 28 x 44.5 U Steel Reinforcement | 1239 |
| Hor | Sash | Door Sash T | 4 | 659 | \ - / | 28 x 44.5 U Steel Reinforcement | 444 |
| Vert | Sash group | French Mullion | 1 | 1371 | [ - ] | 28 x 24 Steel Reinforcement | 1371 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 10.756000 | Metres |
| Glazing Bridge Packer | 26 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |
| Gasket 01 | 16.824 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 5 | Print Info: | 11/5/2026 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 623 | 323 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 474 | 1269 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 474 | 1269 |
| 04 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 623 | 323 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 6 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Vert | Bead | 28mm Bead | 2 | 1804 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 333 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1650 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 646.5 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 650.5 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 405 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1705 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 2 | 1905 | \ - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1705 | \ - Y] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 405 | \ - Y] | | |
| Hor | Frame | | 1 | 1909 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1825 | \ - / | 28 x 44.5 U Steel Reinforcement | 1610 |
| Hor | Sash | Door Sash T | 2 | 821.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 606.5 |
| Hor | Sash | Door Sash T | 2 | 825.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 610.5 |
| Vert | Sash group | French Mullion | 1 | 1738 | [ - ] | 28 x 24 Steel Reinforcement | 1738 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 13.348 | Metres |
| Glazing Bridge Packer | 21 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |
| Gasket 01 | 21.108 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 7 | Print Info: | 11/5/2026 |

| **Glass Required:** | **Qty** | **Width** | **Length** |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 323 | 1794 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 636 | 1640 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 640 | 1640 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 8 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Vert | Bead | 28mm Bead | 2 | 1704 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 233 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1550 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 450.5 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 446.5 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1305 | \ - Y] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 305 | \ - Y] | | |
| Vert | Frame | Frame 6 Chamber | 2 | 1805 | \ - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 305 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1305 | [Y - / | | |
| Hor | Frame | | 1 | 1809 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1725 | \ - / | 28 x 44.5 U Steel Reinforcement | 1510 |
| Hor | Sash | Door Sash T | 2 | 625.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 410.5 |
| Hor | Sash | Door Sash T | 2 | 621.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 406.5 |
| Vert | Sash group | French Mullion | 1 | 1638 | [ - ] | 28 x 24 Steel Reinforcement | 1638 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 11.748 | Metres |
| Glazing Bridge Packer | 21 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |
| Gasket 01 | 18.708 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 9 | Print Info: | 11/5/2026 |

| **Glass Required:** | **Qty** | **Width** | **Length** |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 440 | 1540 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 436 | 1540 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 1694 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 10 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Transom | SPQ-5-30252 78mm |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Transo... | Welded (Standard) |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |
| Vertical Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Hor | Bead | 28mm Bead | 4 | 283 | [ - ] | | |
| Vert | Bead | 28mm Bead | 2 | 1633 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 333 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 1383 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1479 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 521.5 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 525.5 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1805 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 405 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 1705 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1455 | \ - Y] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 355 | \ - Y] | | |
| Vert | Frame | Frame 6 Chamber | 1 | 2105 | \ - / | | |
| Hor | Frame | T Transom/Mullion | 1 | 417 | [Y - > | | |
| Hor | Frame | | 1 | 1707 | < - Y] | | |
| Hor | Frame | T Transom/Mullion | 1 | 404 | < - > | | |
| Hor | Frame | | 1 | 1492 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1654 | \ - / | 28 x 44.5 U Steel Reinforcement | 1439 |
| Hor | Sash | Door Sash T | 2 | 696.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 481.5 |
| Hor | Sash | Door Sash T | 2 | 700.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 485.5 |
| Vert | Sash group | French Mullion | 1 | 1571 | [ - ] | 28 x 24 Steel Reinforcement | 1571 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 16.306 | Metres |
| Glazing Bridge Packer | 31 | Unit |
| French Door End Cap | 2 | Unit |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 11 | Print Info: | 11/5/2026 |


| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Run Up Block | 2 | Unit |
| Gasket 01 | 18.74 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 273 | 323 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 273 | 1623 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 1373 | 323 |
| 04 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 512 | 1469 |
| 05 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 516 | 1469 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 12 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Transom | SPQ-5-30252 78mm |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Transo... | Welded (Standard) |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |
| Vertical Split Position | By Dimensions |

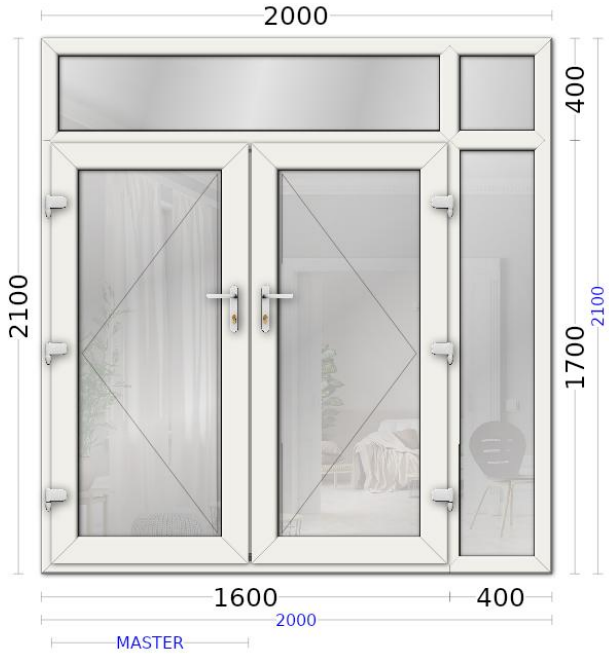


| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Hor | Bead | 28mm Bead | 2 | 1533 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 333 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 333 | [ - ] | | |
| Vert | Bead | 28mm Bead | 2 | 1633 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1479 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 600.5 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 596.5 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 2005 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 2105 | \ - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 405 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1605 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 1705 | \ - Y] | | |
| Vert | Frame | Frame 6 Chamber | 1 | 405 | \ - Y] | | |
| Hor | Frame | T Transom/Mullion | 1 | 415 | [Y - > | | |
| Hor | Frame | | 1 | 1705 | [Y - > | | |
| Hor | Frame | | 1 | 1642 | < - > | | |
| Hor | Frame | T Transom/Mullion | 1 | 454 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1654 | \ - / | 28 x 44.5 U Steel Reinforcement | 1439 |
| Hor | Sash | Door Sash T | 2 | 775.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 560.5 |
| Hor | Sash | Door Sash T | 2 | 771.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 556.5 |
| Vert | Sash group | French Mullion | 1 | 1571 | [ - ] | 28 x 24 Steel Reinforcement | 1571 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 17.106 | Metres |
| Glazing Bridge Packer | 31 | Unit |
| French Door End Cap | 2 | Unit |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 13 | Print Info: | 11/5/2026 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Run Up Block | 2 | Unit |
| Gasket 01 | 19.34 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 1523 | 323 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 590 | 1469 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 586 | 1469 |
| 04 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 323 | 323 |
| 05 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 323 | 1623 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 14 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Transom | SPQ-5-30252 78mm |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Transo... | Welded (Standard) |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |
| Vertical Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Hor | Bead | 28mm Bead | 4 | 333 | [ - ] | | |
| Vert | Bead | 28mm Bead | 2 | 1683 | [ - ] | | |
| Vert | Bead | 28mm Bead | 6 | 283 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 612 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 583 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1529 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 446.5 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 450.5 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1705 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 355 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 1755 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1305 | \ - Y] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 405 | \ - Y] | | |
| Vert | Frame | Frame 6 Chamber | 1 | 2105 | \ - / | | |
| Hor | Frame | T Transom/Mullion | 1 | 367 | [Y - > | | |
| Hor | Frame | | 1 | 1757 | < - Y] | | |
| Hor | Frame | T Transom/Mullion | 1 | 454 | < - > | | |
| Hor | Frame | | 1 | 1342 | < - > | | |
| Hor | Frame | T Transom/Mullion | 1 | 404 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1704 | \ - / | 28 x 44.5 U Steel Reinforcement | 1489 |
| Hor | Sash | Door Sash T | 2 | 621.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 406.5 |
| Hor | Sash | Door Sash T | 2 | 625.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 410.5 |
| Vert | Sash group | French Mullion | 1 | 1621 | [ - ] | 28 x 24 Steel Reinforcement | 1621 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 16.456 | Metres |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 15 | Print Info: | 11/5/2026 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Glazing Bridge Packer | 36 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |
| Gasket 01 | 18.54 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 323 | 273 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 323 | 1673 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 602 | 273 |
| 04 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 436 | 1519 |
| 05 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 440 | 1519 |
| 06 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 573 | 273 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 16 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Transom | SPQ-5-30252 78mm |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Transo... | Welded (Standard) |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |
| Vertical Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Hor | Bead | 28mm Bead | 4 | 333 | [ - ] | | |
| Vert | Bead | 28mm Bead | 2 | 1683 | [ - ] | | |
| Vert | Bead | 28mm Bead | 6 | 283 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 1133 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 38 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1529 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 400.5 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 396.5 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1605 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 2105 | \ - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 405 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1205 | [Y - / | | |
| Vert | Frame | Frame 6 Chamber | 1 | 1755 | \ - Y] | | |
| Vert | Frame | Frame 6 Chamber | 1 | 355 | \ - Y] | | |
| Hor | Frame | T Transom/Mullion | 1 | 365 | [Y - > | | |
| Hor | Frame | | 1 | 1757 | [Y - > | | |
| Hor | Frame | | 1 | 37.5 | < - None | | |
| Hor | Frame | T Transom/Mullion | 1 | 454 | < - > | | |
| Hor | Frame | T Transom/Mullion | 1 | 404 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1704 | \ - / | 28 x 44.5 U Steel Reinforcement | 1489 |
| Hor | Sash | Door Sash T | 2 | 575.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 360.5 |
| Hor | Sash | Door Sash T | 2 | 571.5 | \ - / | 28 x 44.5 U Steel Reinforcement | 356.5 |
| Vert | Sash group | French Mullion | 1 | 1621 | [ - ] | 28 x 24 Steel Reinforcement | 1621 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 16.248001 | Metres |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 17 | Print Info: | 11/5/2026 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Glazing Bridge Packer | 36 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |
| Gasket 01 | 18.14 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 1123 | 273 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 390 | 1519 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 386 | 1519 |
| 04 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 323 | 273 |
| 05 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 48 | 273 |
| 06 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 323 | 1673 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 18 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Vert | Bead | 28mm Bead | 4 | 2004 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 233 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1850 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 413 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 2 | 305 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 2 | 1205 | [Y - Y] | | |
| Hor | Frame | Frame 6 Chamber | 2 | 305 | \ - Y] | | |
| Vert | Frame | Frame 6 Chamber | 2 | 2105 | \ - / | | |
| Hor | Frame | | 2 | 2109 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 2025 | \ - / | 28 x 44.5 U Steel Reinforcement | 1810 |
| Hor | Sash | Door Sash T | 4 | 588 | \ - / | 28 x 44.5 U Steel Reinforcement | 373 |
| Vert | Sash group | French Mullion | 1 | 1938 | [ - ] | 28 x 24 Steel Reinforcement | 1938 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 17.84 | Metres |
| Glazing Bridge Packer | 26 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |
| Gasket 01 | 20.824 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 1994 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 403 | 1840 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 19 | Print Info: | 11/5/2026 |

| **Glass Required:** | **Qty** | **Width** | **Length** |
|---|---|---|---|
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 403 | 1840 |
| 04 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 1994 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 20 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Transom | SPQ-5-30252 78mm |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Transo... | Welded (Standard) |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |
| Vertical Split Position | By Dimensions |




| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Hor | Bead | 28mm Bead | 8 | 233 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1483 | [ - ] | | |
| Vert | Bead | 28mm Bead | 6 | 283 | [ - ] | | |
| Hor | Bead | 28mm Bead | 2 | 1162 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1329 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 413 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1805 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 2 | 1905 | \ - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 305 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1205 | [Y - Y] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 305 | \ - Y] | | |
| Hor | Frame | T Transom/Mullion | 1 | 367 | [Y - > | | |
| Hor | Frame | | 1 | 1557 | < - Y] | | |
| Hor | Frame | T Transom/Mullion | 1 | 365 | [Y - > | | |
| Hor | Frame | | 1 | 1555 | [Y - > | | |
| Hor | Frame | T Transom/Mullion | 2 | 354 | < - > | | |
| Hor | Frame | | 1 | 1275 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1504 | \ - / | 28 x 44.5 U Steel Reinforcement | 1289 |
| Hor | Sash | Door Sash T | 4 | 588 | \ - / | 28 x 44.5 U Steel Reinforcement | 373 |
| Vert | Sash group | French Mullion | 1 | 1421 | [ - ] | 28 x 24 Steel Reinforcement | 1421 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 18.506 | Metres |
| Glazing Bridge Packer | 41 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 21 | Print Info: | 11/5/2026 |


| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 01 | 16.656 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 273 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 1473 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 1152 | 273 |
| 04 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 403 | 1319 |
| 05 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 403 | 1319 |
| 06 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 273 |
| 07 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 1473 |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 22 | Print Info: | 11/5/2026 |

| Main Options | |
|---|---|
| Colour (External) | White [SP] |
| Colour (Internal) | White [SP] |
| Frame (Standard) (Top) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Bottom) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Left) | SPQ-6-11252 68mm 6 Chamber |
| Frame (Standard) (Right) | SPQ-6-11252 68mm 6 Chamber |
| Transom | SPQ-5-30252 78mm |
| Mullion | SPQ-5-30252 78mm |
| Joint (Structural T/Z) (Transo... | Welded (Standard) |
| Joint (Structural T/Z) (Mullion) | Welded (Standard) |
| Bead | 28mm |
| Cylinder | Brass Cylinder |
| Handle (Door) | White Handle Lever/Lever (Short Backplate) |
| Hinge (Door) | Flag Hinge |
| Hinge Colour (Door) | White Flag Hinge |
| Hinge Position (Door) | 3 Hinges |
| Lock (Door) (Double Door) | Standard Door Lock |
| Glazing Method | Glazed |
| Glass Type | 4-20-4 Clear Tuff Low E |
| Glass Gas Fill | Argon |
| Opening Direction | Open Out |
| Master Leaf | Left |
| Component Type | Glass |
| Drainage | Concealed Drainage |
| Location | Please Specify |
| Horizontal Split Position | By Dimensions |
| Vertical Split Position | By Dimensions |

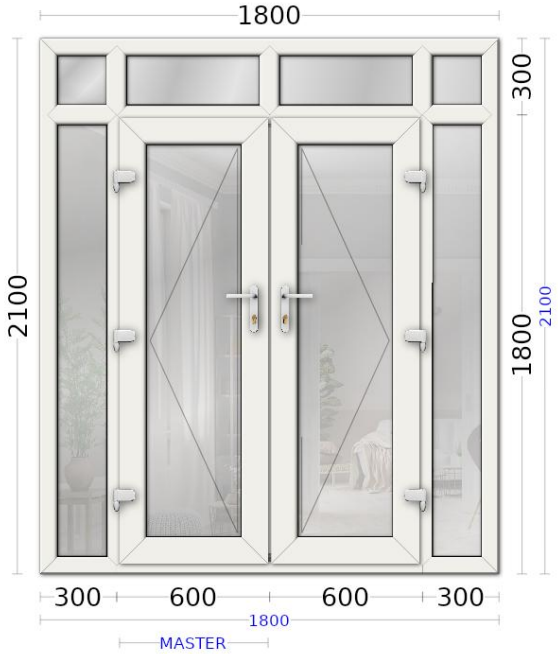


| Sections Required: | | | Qty | Length | End Prep | Reinforcing | Length |
|---|---|---|---|---|---|---|---|
| Hor | Bead | 28mm Bead | 8 | 233 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1733 | [ - ] | | |
| Vert | Bead | 28mm Bead | 8 | 233 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 562 | [ - ] | | |
| Vert | Bead | 28mm Bead | 4 | 1579 | [ - ] | | |
| Hor | Bead | 28mm Bead | 4 | 413 | [ - ] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1805 | \ - / | | |
| Vert | Frame | Frame 6 Chamber | 2 | 2105 | \ - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 305 | [Y - / | | |
| Hor | Frame | Frame 6 Chamber | 1 | 1205 | [Y - Y] | | |
| Hor | Frame | Frame 6 Chamber | 1 | 305 | \ - Y] | | |
| Hor | Frame | T Transom/Mullion | 1 | 317 | [Y - > | | |
| Hor | Frame | | 1 | 1807 | < - Y] | | |
| Hor | Frame | T Transom/Mullion | 1 | 315 | [Y - > | | |
| Hor | Frame | | 1 | 1805 | [Y - > | | |
| Hor | Frame | T Transom/Mullion | 3 | 354 | < - > | | |
| Hor | Frame | | 1 | 1275 | < - > | | |
| Vert | Sash | Door Sash T | 4 | 1754 | \ - / | 28 x 44.5 U Steel Reinforcement | 1539 |
| Hor | Sash | Door Sash T | 4 | 588 | \ - / | 28 x 44.5 U Steel Reinforcement | 373 |
| Vert | Sash group | French Mullion | 1 | 1671 | [ - ] | 28 x 24 Steel Reinforcement | 1671 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 02 | 20.556 | Metres |
| Glazing Bridge Packer | 46 | Unit |
| French Door End Cap | 2 | Unit |
| Run Up Block | 2 | Unit |

# WORK ORDER

| | | | | |
|---|---|---|---|---|
| Customer: | Test Customer | | Input Info: | 11/5/2026 |
| Reference: | Ambrish French Door | SupplyAndFit | | |
| Job No: | 340 | Page 23 | Print Info: | 11/5/2026 |

| Accessories Required: | Qty | Unit Of Measurement |
|---|---|---|
| Gasket 01 | 18.656 | Metres |
| White Handle Lever/Lever (Short Backplate) | 2 | Unit |
| Flag Hinge White | 6 | Unit |
| L/H Keep Set | 1 | Unit |
| Standard Door Lock | 1 | Unit |
| Brass Cylinder | 2 | Unit |
| Double Shootbolt Keep Set | 1 | Unit |
| Standard Slave Door Lock | 1 | Unit |

| Glass Required: | Qty | Width | Length |
|---|---|---|---|
| 01 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 223 |
| 02 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 1723 |
| 03 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 552 | 223 |
| 04 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 403 | 1569 |
| 05 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 403 | 1569 |
| 06 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 552 | 223 |
| 07 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 223 |
| 08 (Frame-01) 4-20-4 Clear Tuff Low E : Thermal Spacer Bar | 1 | 223 | 1723 |
